


ALSTOM PPL RELOCATION
TOBEY ROAD SITE
Rev 2.13

ID		Task Name	Duration	Start	Finish	Predecessors	Resource Names	2014											
								Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec
1		Purchase 44 Tobey Rd	23.4 wks	Wed 5/15/13	Fri 10/25/13														
2		Tobey Rd Negotiations	3 wks	Wed 5/15/13	Tue 6/4/13		Alstom												
3		Purchase Sale Agreement	0 wks	Fri 6/14/13	Fri 6/14/13	2	Alstom												
4		Phase 1/2 Environmental	4 wks	Mon 6/17/13	Fri 7/12/13	3	JNH												
5		Asbestos Review	4 wks	Mon 6/17/13	Fri 7/12/13	3	JNH												
6		Ground Water Survey	3 wks	Mon 6/24/13	Fri 7/12/13	3	Hesketh/well driller												
7		Site Geotech	2 wks	Mon 6/17/13	Fri 6/28/13	3	Hesketh/Welti												
8		Title Insurance	6 wks	Mon 6/17/13	Fri 7/26/13	3	Alstom												
9		Close Property	0 wks	Fri 10/25/13	Fri 10/25/13	22,3,4,5,8	Alstom												
10		Environ Permitting	49 wks	Mon 6/17/13	Fri 5/23/14														
11		Air DEEP Application	2 wks	Mon 6/17/13	Fri 6/28/13	24	Vin Romano												
12		Submit	0 wks	Fri 6/28/13	Fri 6/28/13	11	Vin Romano												
13		Modeling Complete	10 wks	Mon 9/9/13	Fri 11/15/13	12	Amec												
14		Submit to DEEP	1 wk	Mon 11/18/13	Fri 11/22/13	13	Vin Romano												
15		Air Permit Approved	26 wks	Mon 11/25/13	Fri 5/23/14	12,13	DEEP/Amec/Romano												
16		Site Plan Development	22 wks	Mon 6/3/13	Fri 11/1/13														
17		Property Survey	3 wks	Mon 6/3/13	Fri 6/21/13		Hesketh												
18		Site Plan Design	7 wks	Mon 6/24/13	Fri 8/9/13	17,24	Hesketh												
19		Submit to Bloomfield	13.2 wks	Fri 8/2/13	Fri 11/1/13		Hesketh												
20		Bloomfield Inland Wetlands	0 wks	Mon 9/16/13	Mon 9/16/13	19	Bloomfield												
21		Bloomfield TP&Z Mtg	0 wks	Thu 9/26/13	Thu 9/26/13	20	Bloomfield												
22		Site Plan Approval	0 wks	Thu 9/26/13	Thu 9/26/13	21,20	Bloomfield												
23		Engineering Restart	27.4 wks	Mon 6/3/13	Tue 12/10/13														
24		Develop Bldg/Site Gas	2 wks	Mon 6/3/13	Fri 6/14/13		Alstom/Avakian												
25		Waldron GA Review	1 wk	Mon 6/17/13	Fri 6/21/13	24	Alstom/Avakian/Waldron												
26		Waldron Proposal Dev	2 wks	Mon 6/17/13	Fri 6/28/13		Waldron												
27		Award Contract	1.2 wks	Mon 7/1/13	Mon 7/8/13	26	Alstom												
28		Process ME&P Design	16.4 wks	Tue 7/9/13	Wed 10/30/13	27	Waldron												
29		Structural Design	17.4 wks	Mon 7/15/13	Tue 11/12/13		Waldron												
30		Building ME&P	8 wks	Tue 8/6/13	Mon 9/30/13		EDM												
31		Architect	8 wks	Tue 8/6/13	Mon 9/30/13		SLAM												
32		Structural Peer Review	4 wks	Wed 11/13/13	Tue 12/10/13	29	SLAM												
33		CL Dis/Re Assembly	13.8 wks	Mon 5/20/13	Thu 8/22/13														
34		Prepare RFP	2 wks	Mon 5/20/13	Fri 5/31/13		Alstom												
35		Out for Bid	3 wks	Mon 5/20/13	Fri 6/7/13		Cianbro/AP Com												
36		Bid Review	6 wks	Fri 6/28/13	Thu 8/8/13		Alstom												
37		Award Contract	2 wks	Fri 8/9/13	Thu 8/22/13	36	Alstom												
38		SITE/CIVIL/CONC/DEMO	74 wks	Mon 7/8/13	Fri 12/5/14														
39		ID/interview contractors	3 wks	Mon 7/8/13	Fri 7/26/13		Alstom/Avakian												
40		Develop RFP	8 wks	Mon 8/12/13	Fri 10/4/13	18	Alstom/Avakian												
41		Out for Bid	4.2 wks	Fri 10/18/13	Fri 11/15/13	22FS+1 wk,40,39	Bldg/Site GC												
42		General	3.2 wks	Thu 12/19/13	Thu 1/9/14														
43		Award Contract	0 wks	Thu 12/19/13	Thu 12/19/13	22	Alstom												
44		Mobilize	1 wk	Fri 1/3/14	Thu 1/9/14		PDS												
45		Site Work	34 wks	Tue 1/7/14	Mon 9/1/14		PDS												
46		Water lines	1 wk	Mon 4/21/14	Fri 4/25/14	57													
47		E&S Control	0.6 wks	Tue 1/7/14	Thu 1/9/14														
48		Clear/Grub	1 wk	Fri 1/10/14	Thu 1/16/14														
49		Strip/pile TopSoil	2 wks	Tue 1/7/14	Mon 1/20/14														
50		Saw/Rem Pvmt	3 wks	Tue 1/7/14	Mon 1/27/14														
51		Storm Drain	13 wks	Mon 1/20/14	Fri 4/18/14														

ALSTOM PPL RELOCATION
TOBEY ROAD SITE
Rev 2.13

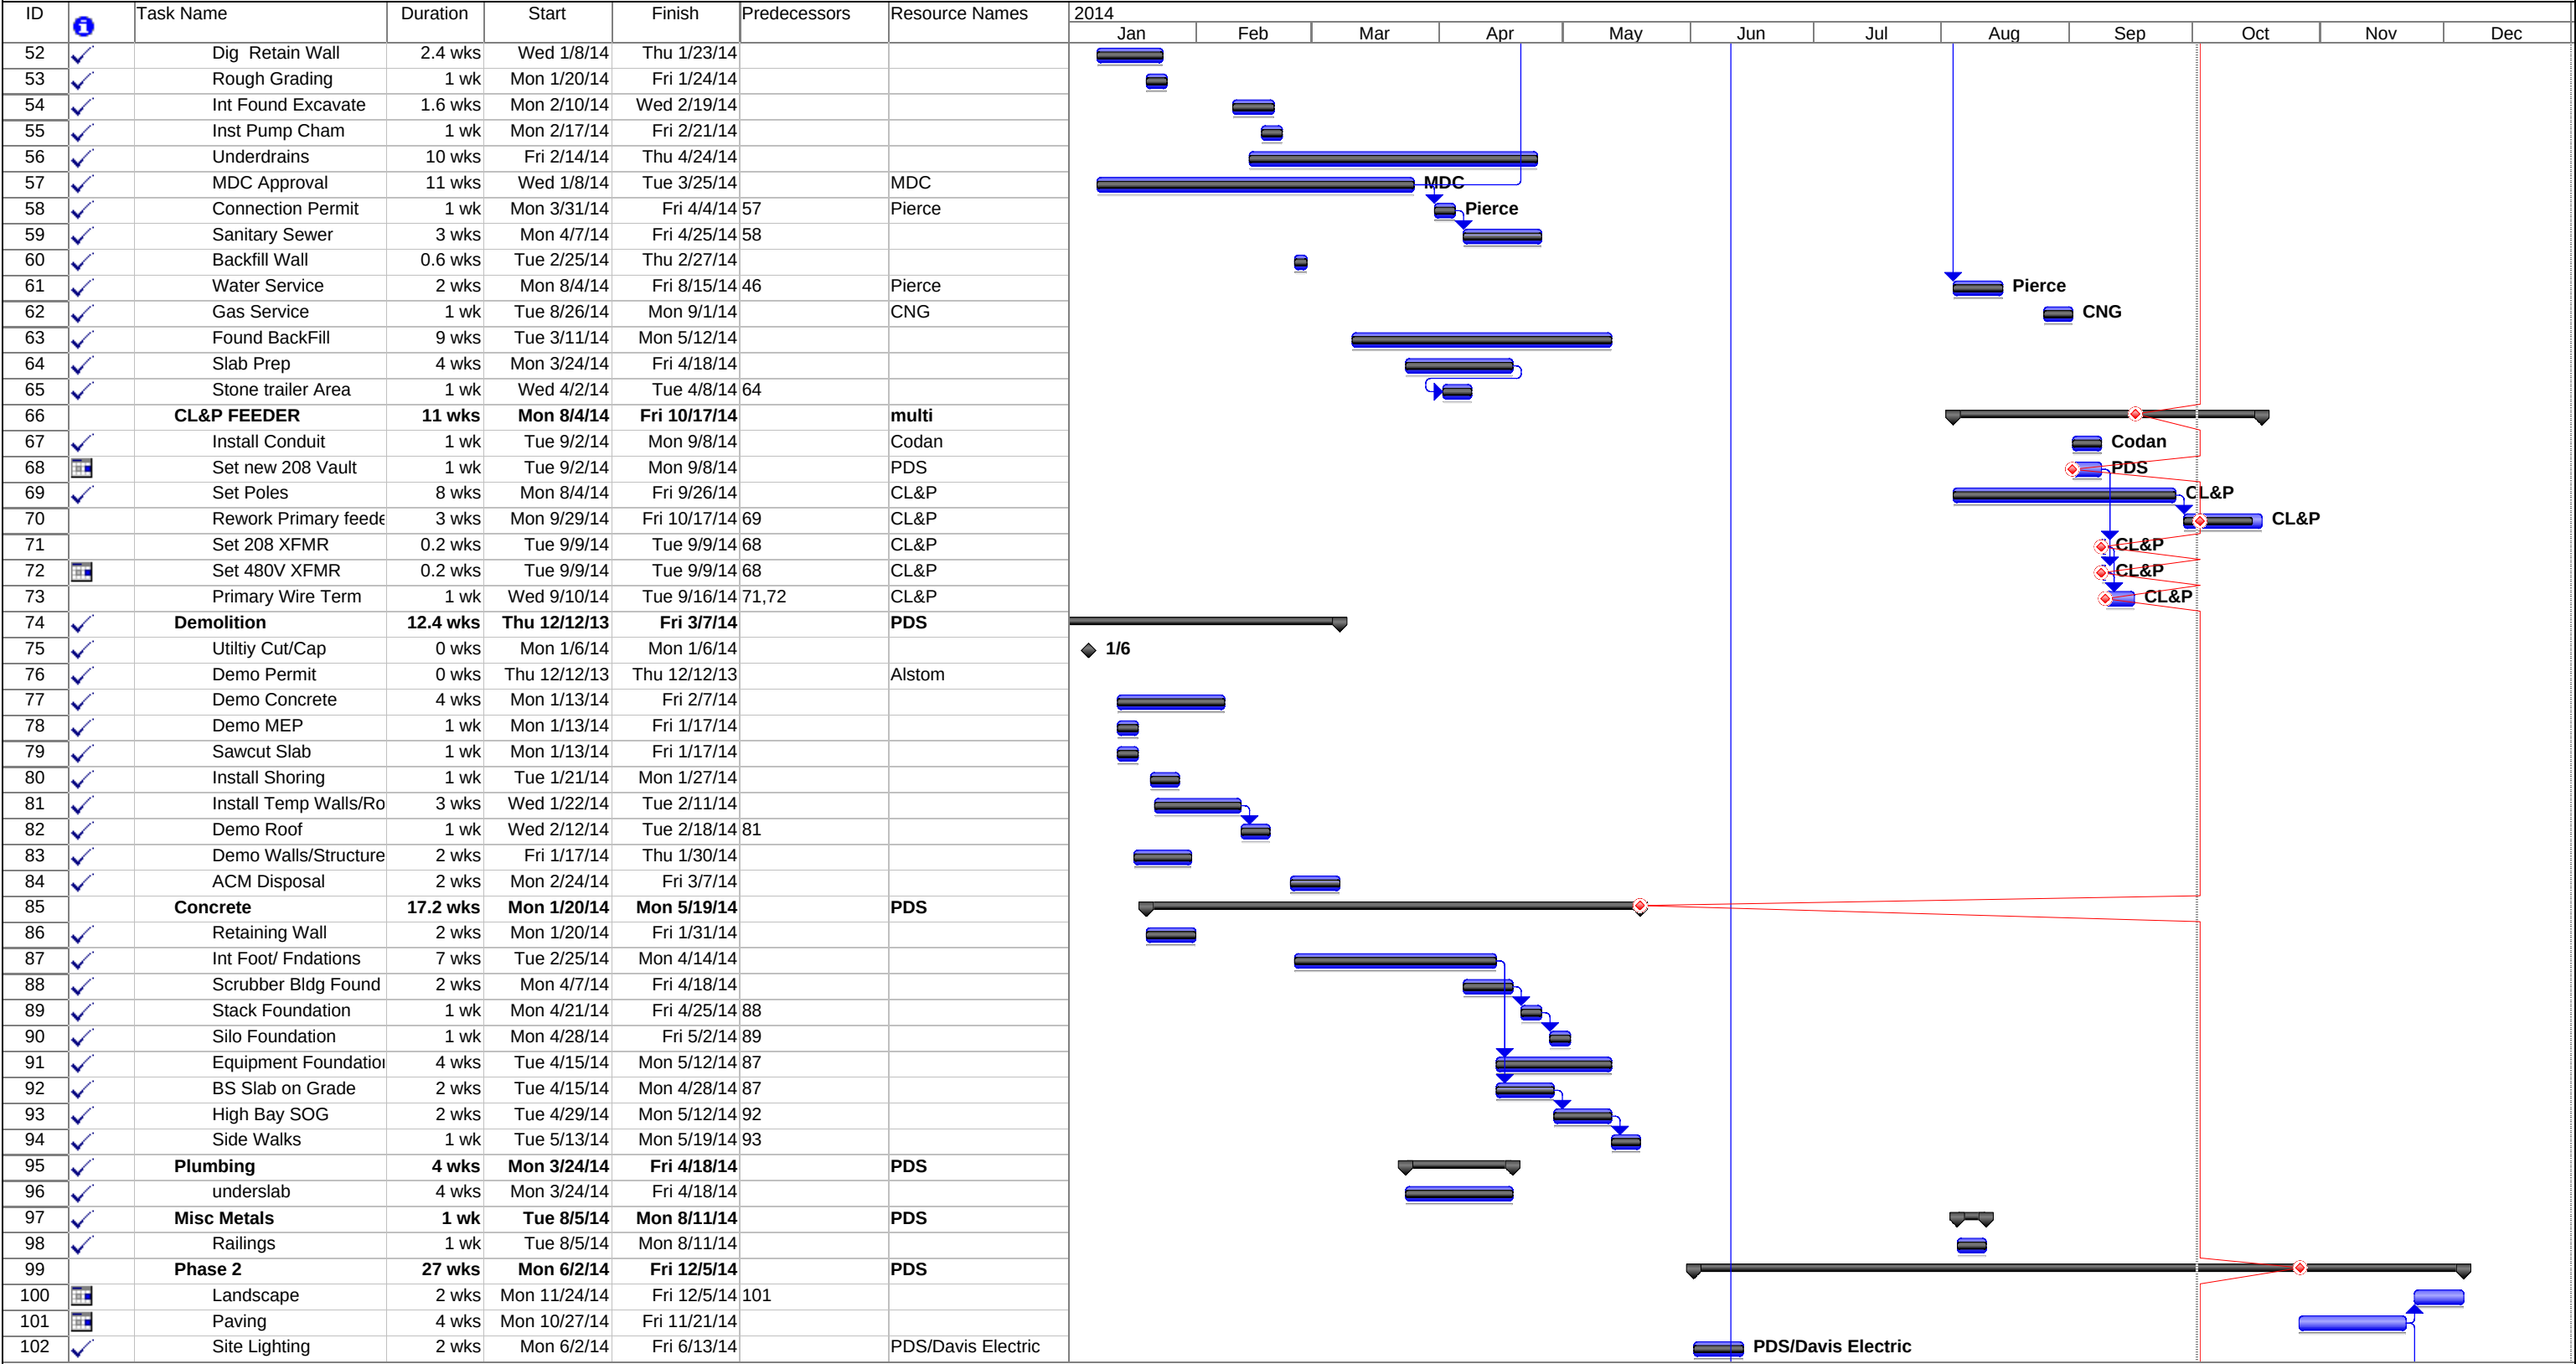

Project: Alstom Test Facility Relocation
Date: Thu 10/2/14

Task
Split



Progress
Milestone



Summary
Project Summary




External Tasks
External Milestone



Deadline



ALSTOM PPL RELOCATION
TOBEY ROAD SITE
Rev 2.13

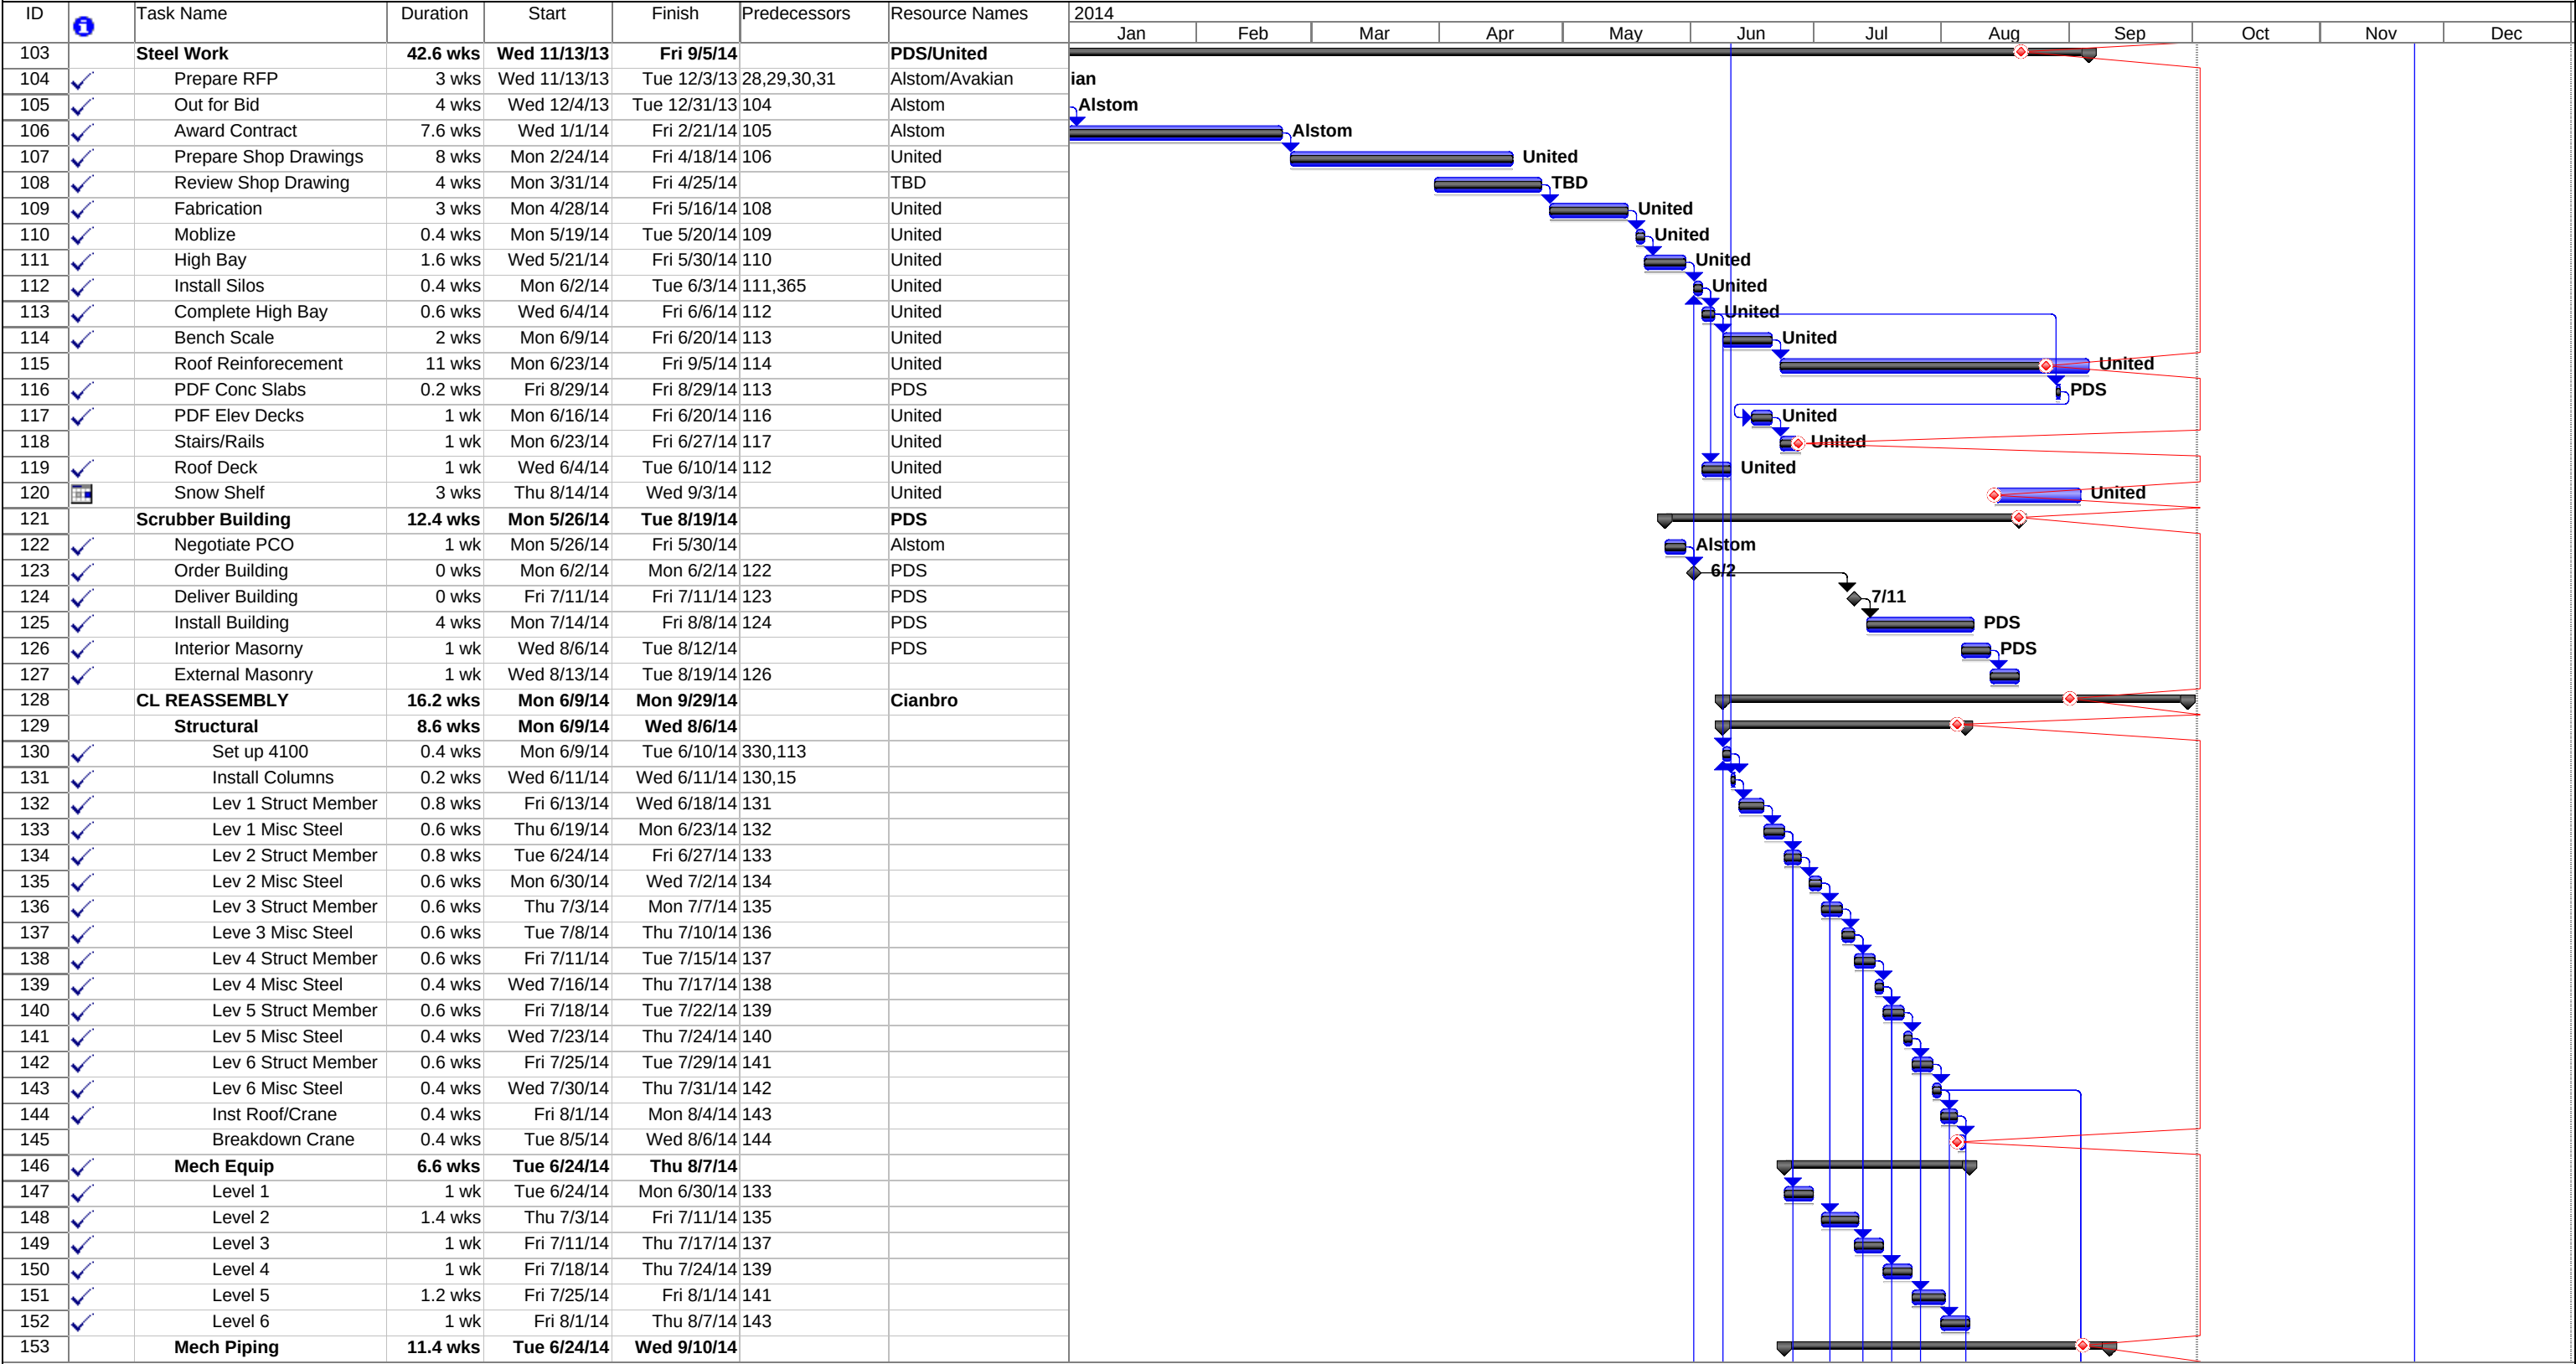

Project: Alstom Test Facility Relocation
Date: Thu 10/2/14

Task
Split



Progress
Milestone



Summary
Project Summary




External Tasks
External Milestone



Deadline



ALSTOM PPL RELOCATION
TOBEY ROAD SITE
Rev 2.13

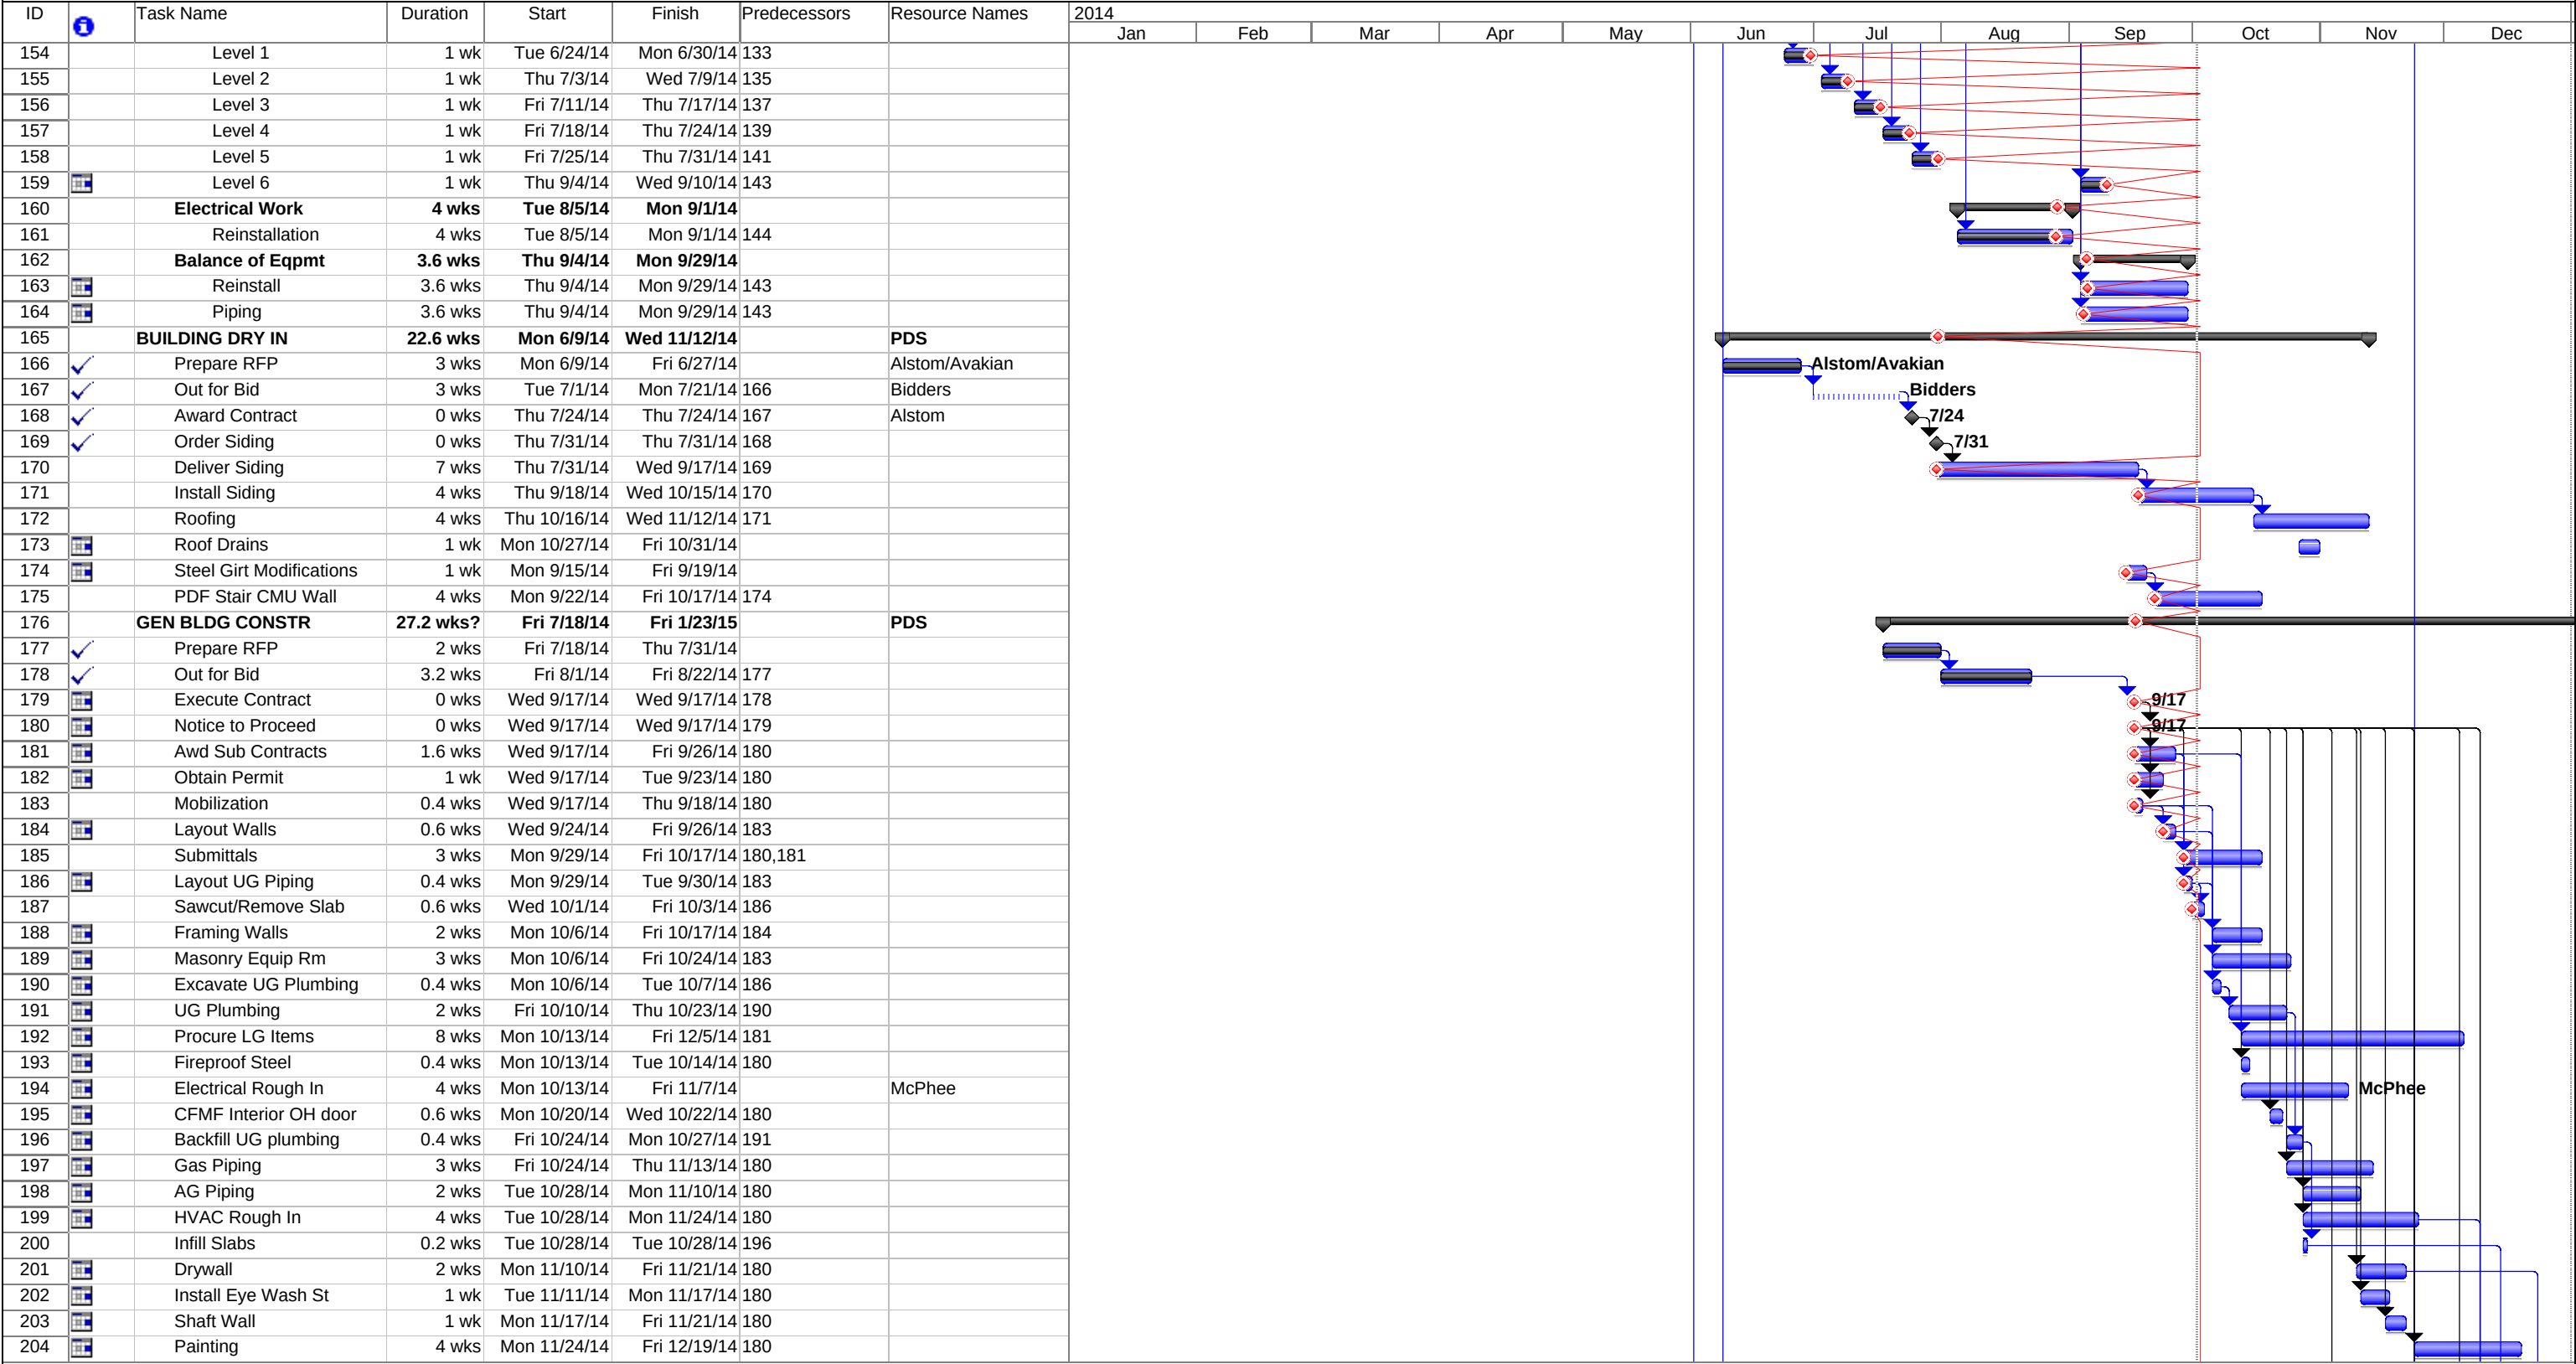


Project: Alstom Test Facility Relocation
Date: Thu 10/2/14

Task
Split



Progress
Milestone



Summary
Project Summary




External Tasks
External Milestone



Deadline



ALSTOM PPL RELOCATION
TOBEY ROAD SITE
Rev 2.13

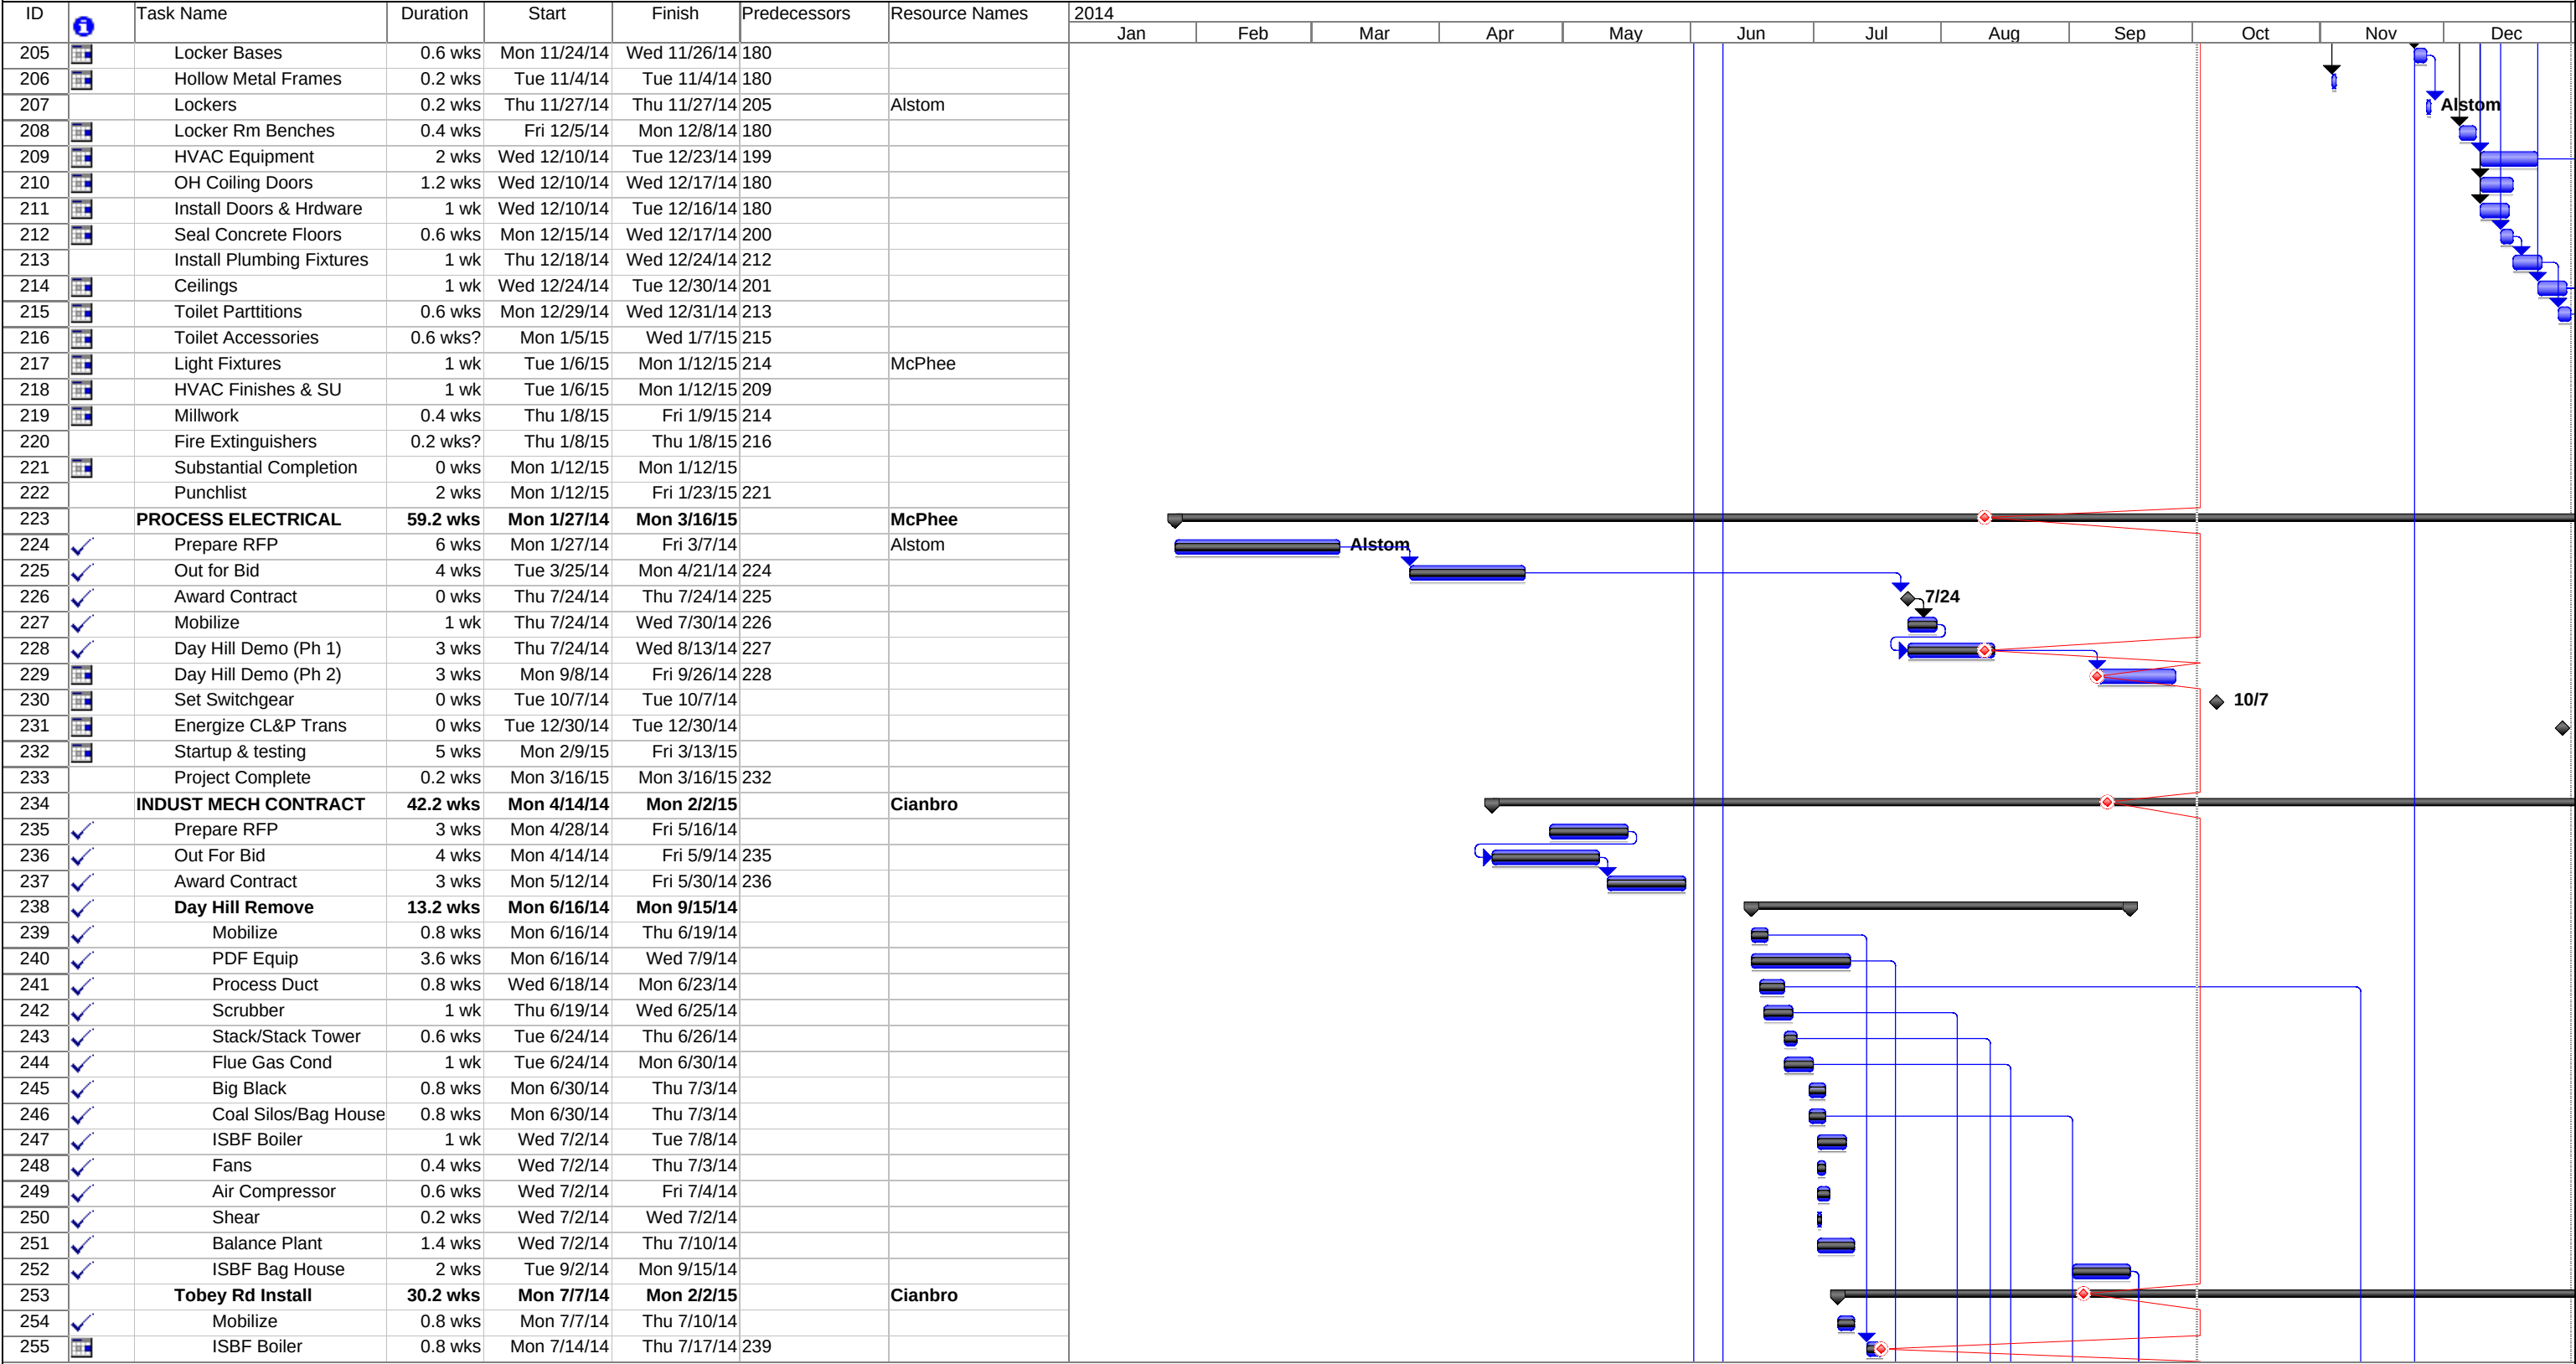

Project: Alstom Test Facility Relocation
Date: Thu 10/2/14

Task
Split

Progress
Milestone


Summary
Project Summary

External Tasks
External Milestone

Deadline



ALSTOM PPL RELOCATION
TOBEY ROAD SITE
Rev 2.13

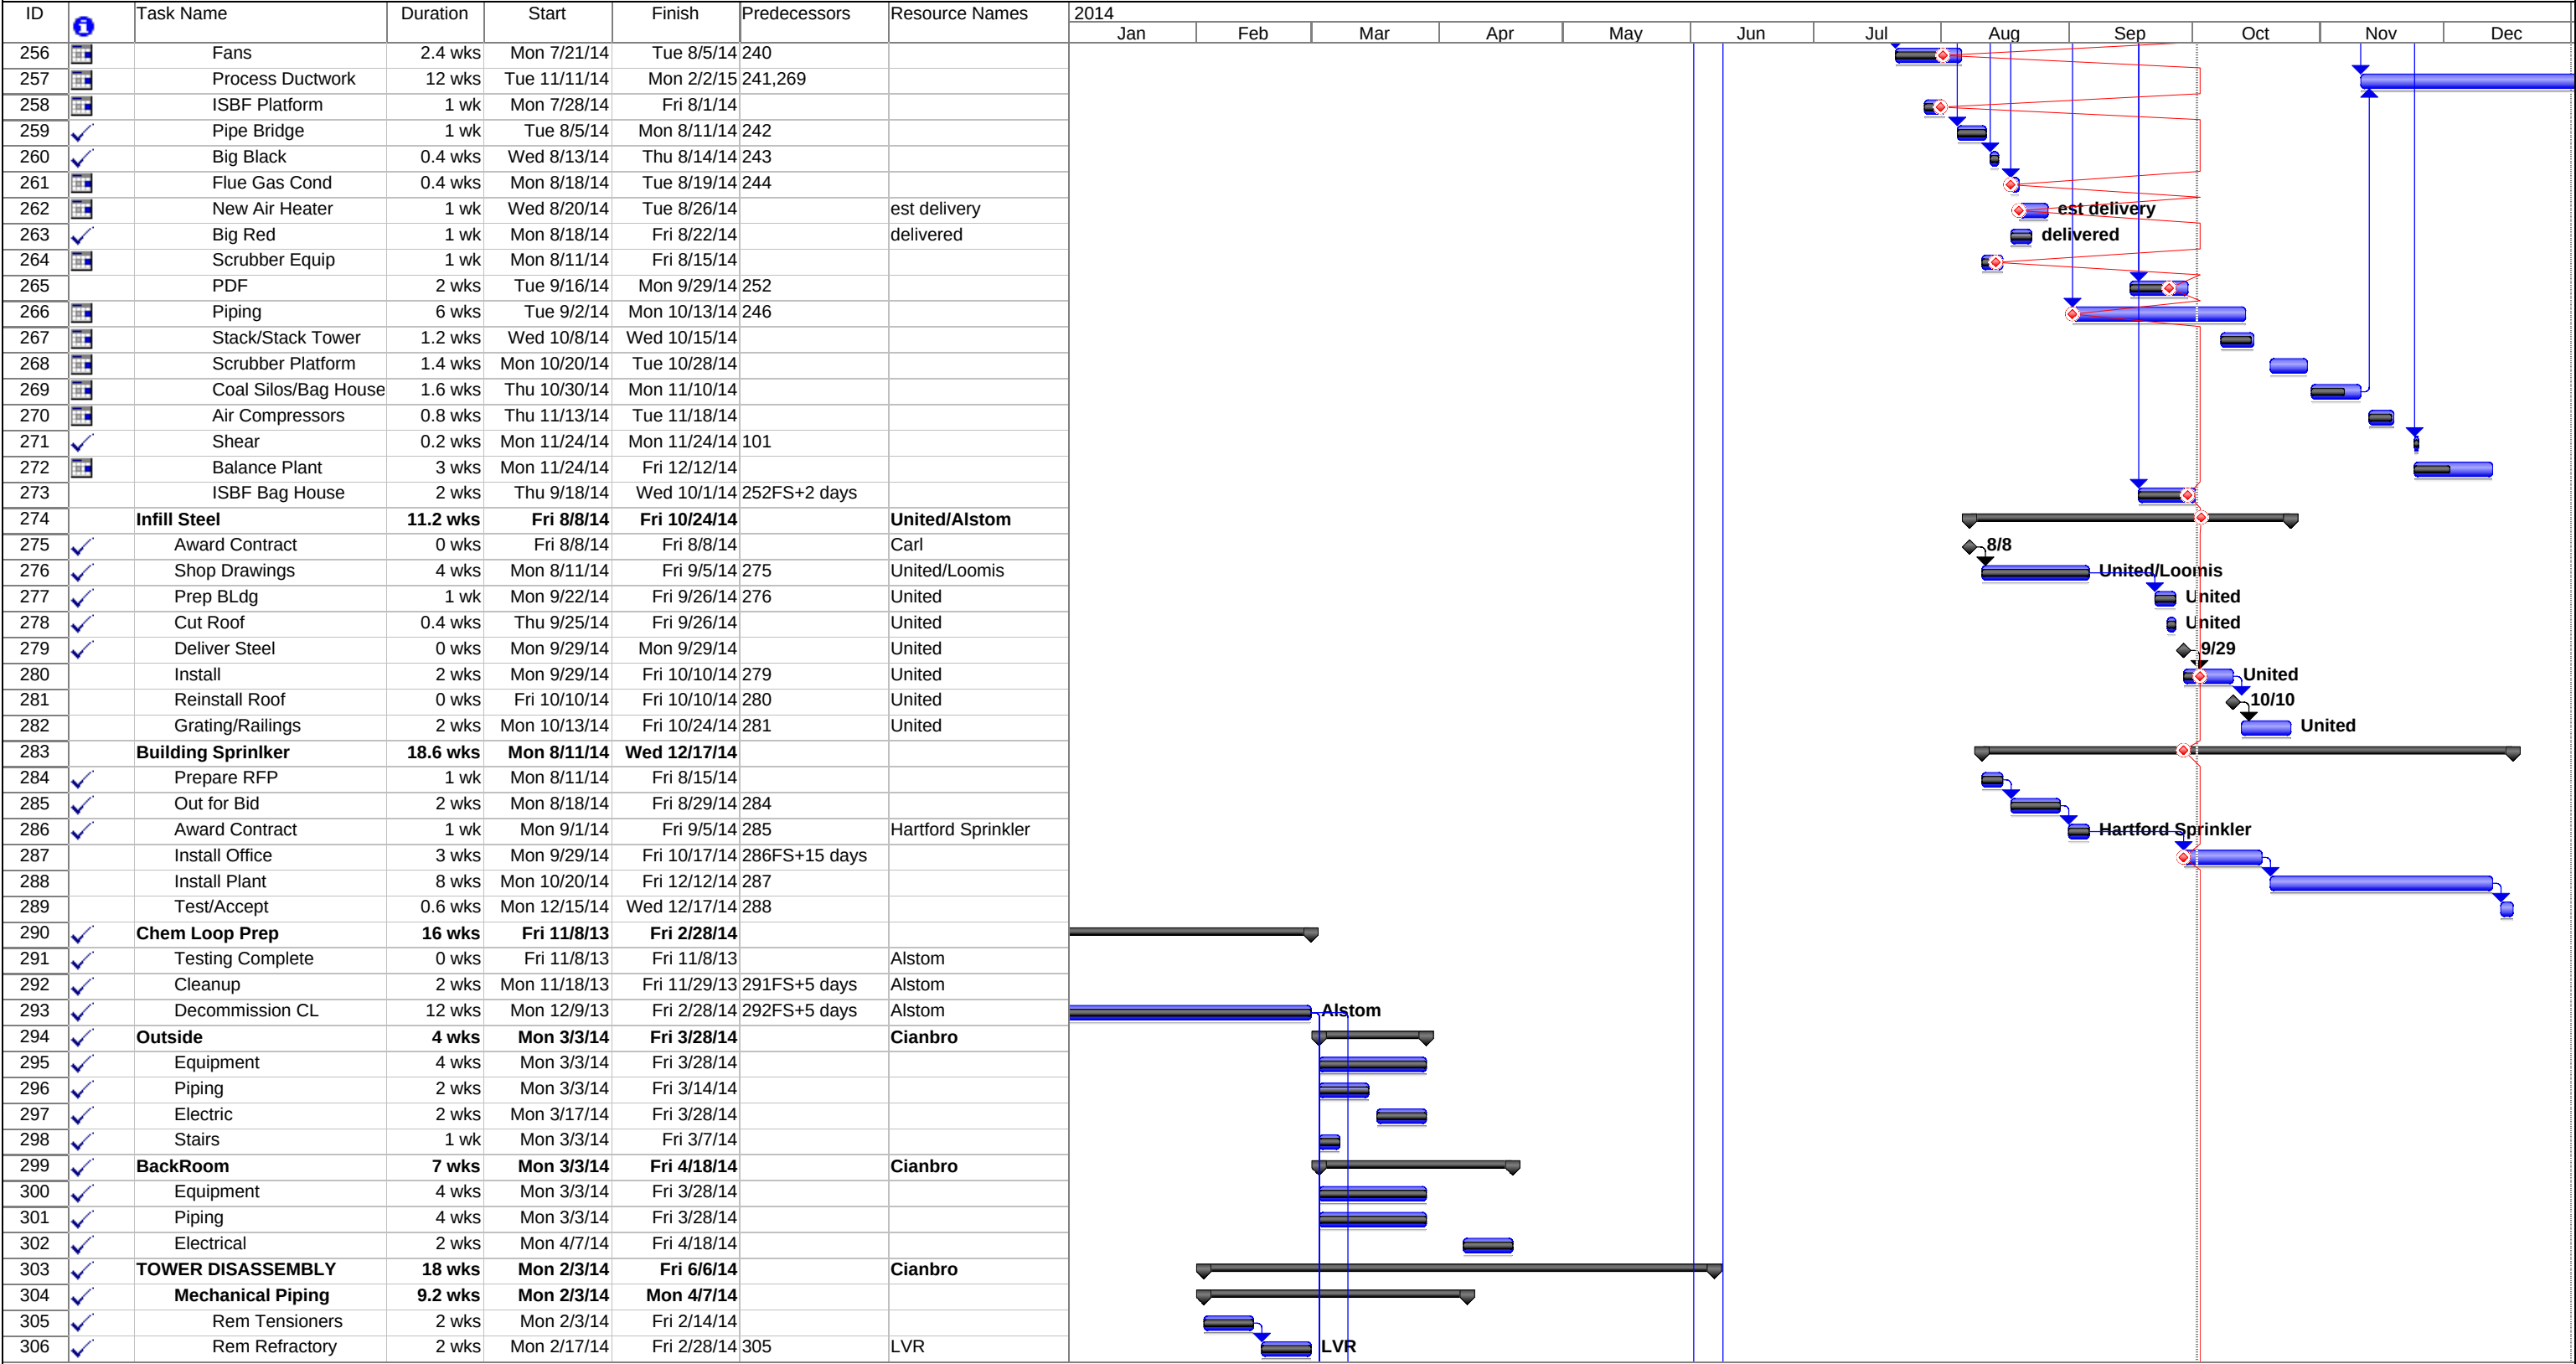

Project: Alstom Test Facility Relocation
Date: Thu 10/2/14

Task
Split



Progress
Milestone



Summary
Project Summary




External Tasks
External Milestone



Deadline



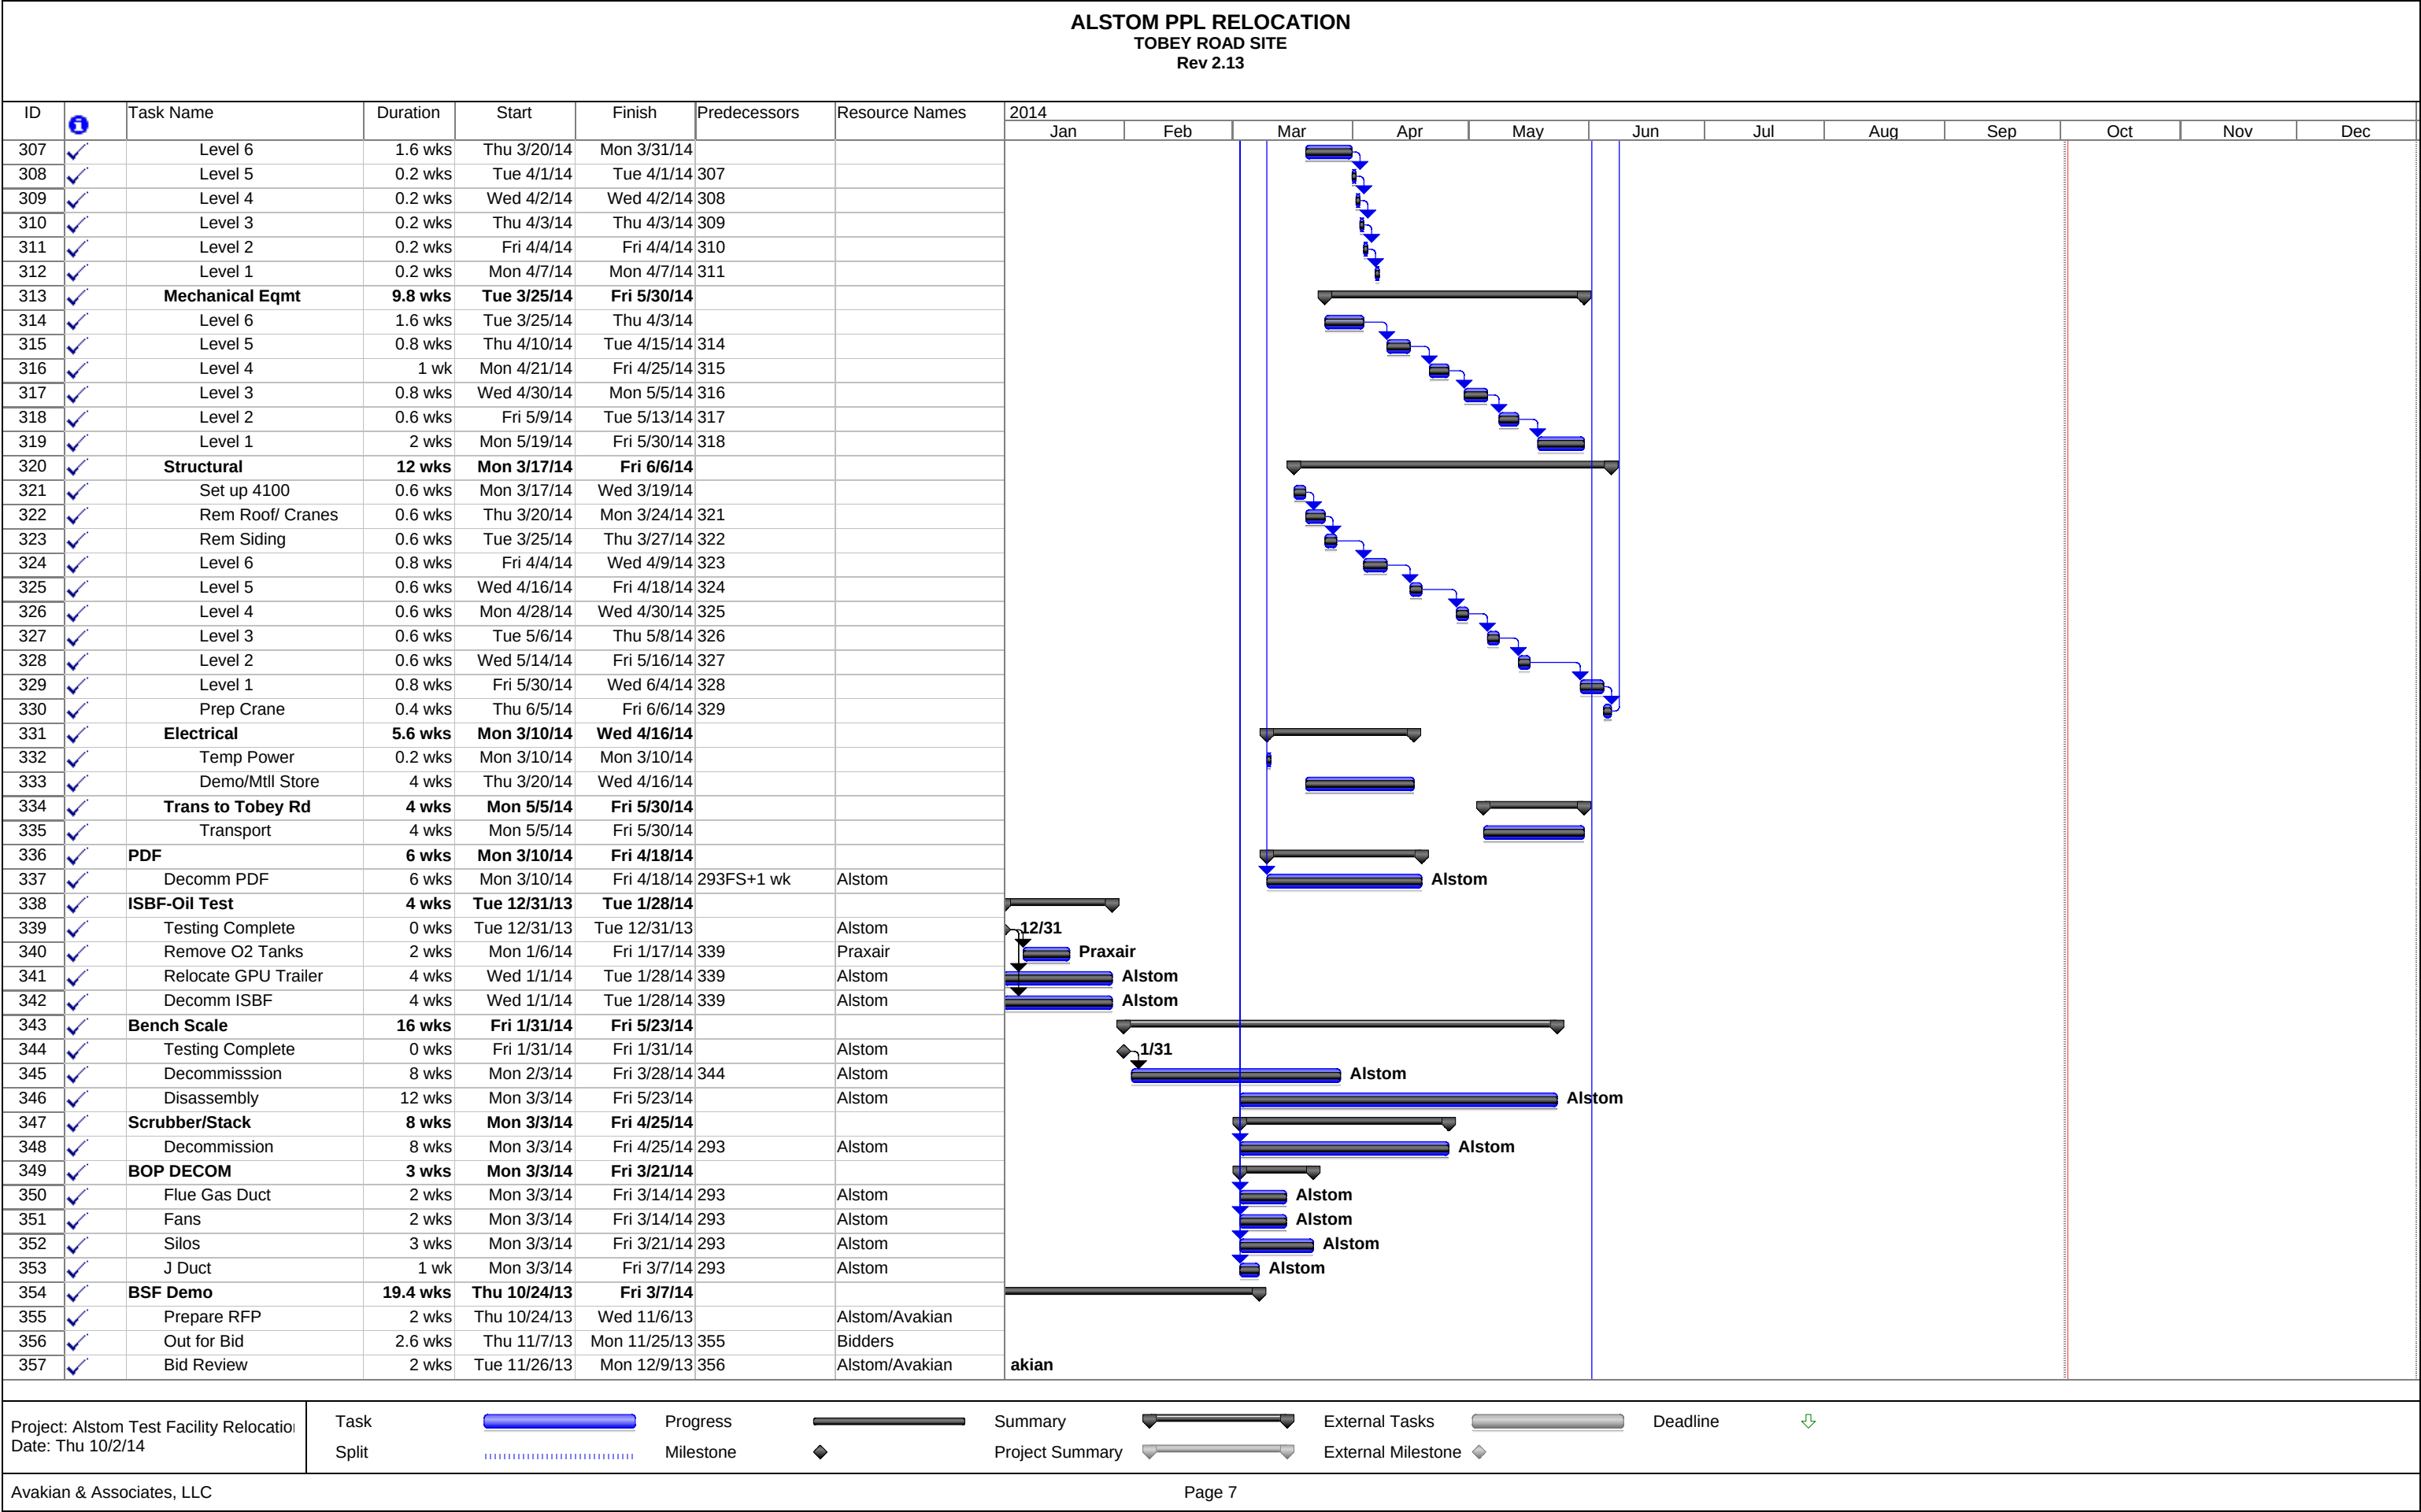

ALSTOM PPL RELOCATION
TOBEY ROAD SITE
Rev 2.13

ID		Task Name	Duration	Start	Finish	Predecessors	Resource Names	2014											
								Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec
358		Award Contract	2 wks	Tue 12/10/13	Mon 12/23/13	357	Alstom	tom											
359		Demo Permit	2 wks	Wed 1/22/14	Tue 2/4/14		Manafort			Manafort									
360		BSF Demo	4 wks	Mon 2/10/14	Fri 3/7/14		Manafort			Manafort									
361		Remove PDF Silos	4.6 wks	Fri 4/11/14	Tue 5/13/14		Cianbro												
362		Award Contract	0 wks	Fri 4/11/14	Fri 4/11/14		Cianbro												
363		Moblize	0.4 wks	Fri 4/25/14	Mon 4/28/14	362FS+2 wks	Cianbro												
364		Remove	2 wks	Tue 4/29/14	Mon 5/12/14	363	Cianbro												
365		Transport to Tobey	0.2 wks	Tue 5/13/14	Tue 5/13/14	364	Cianbro												

Project: Alstom Test Facility Relocation
Date: Thu 10/2/14

Task



Progress



Summary



External Tasks



Deadline



Split



Milestone



Project Summary



External Milestone

